


FACTS AND FIGURES

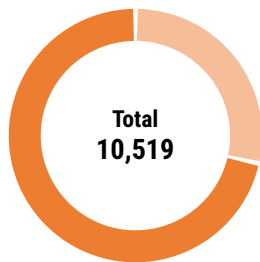

Damage Status - Private Structures

MAJOR HOUSING TYPOLOGIES

Typology	Municipal	District
Stone and Mud Mortar Masonry	80.59%	44.19%
Adobe Structures	10.54%	2.85%
Brick and Cement Mortar Masonry	4.59%	26.60%
Reinforced Cement Concrete (RCC) Frame	1.71%	5.22%
Others	2.56%	21.13%

CBS damage assessment survey, 2015

HOUSING RECONSTRUCTION & RETROFIT UPDATES

Reconstruction Status

Total Eligible HHs	6,919
PA Agreement	6,072 847
I st Tranche received	5,319 1,600
II nd Tranche received	4,044 2,875
III rd Tranche received	2,743 4,176

Houses

Under Construction: 5,271

Completed: 2,700

Retrofitting Status

Total Eligible HHs	1,369
PA Agreement	655 714
I st Tranche received	651 718
II nd Tranche received	1,369

Grievances

Registered: 2,658

Addressed: 2,658

Non-compliances

Registered: 267

Addressed: 238

Data Updated on: 2019-04-22 00:00:00

PO Presence

Active: BC (Shelter), CARE-N (Hygiene), PIN (Shelter)

Phased Out: CHOICE (Health), DCA (Shelter), DCA (Hygiene), ICCO (Agriculture), ICCO (DRM), LUMANTI (Education), LUMANTI (Shelter), LUMANTI (Urban Housings), LUMANTI (Hygiene), LWR (Shelter), NRCS (Agriculture), NRCS (Livelihood), NRCS (Health), NRCS (Shelter), NRCS (Hygiene), PLAN (Education), PLAN (GESI), PLAN (Shelter), PLAN (Social Protection), PLAN (Hygiene), Tearfund (DRM), Tearfund (Education), Tearfund (Livelihood), Tearfund (GESI), Tearfund (Nutrition), Tearfund (Shelter), Tearfund (Social Protection), Tearfund (Hygiene)

OTHER SECTORS



Schools

Damaged: 39
Under Construction: 14
Construction Completed: 14



Health Posts

Damaged: -
Under Construction: -
Construction Completed: -

STATUS OF CONSTRUCTION MATERIALS

Materials	Unit	Req. Quantity*	Ava.	Cost (NRs.)**
Stone	m ³	110,482	-	-
Aggregate	m ³	110,939	-	-
Sand	m ³	11,778	-	-
Timber	cu. ft.	13,521	-	-
Cement (PPC)	Sack	-	-	-
Cement (OPC)	Sack	370,327	-	-
Rebars	kgs.	1,204,388	-	-
Tin	bundle	15,145	-	-
Bricks	pcs.	1,627,026	-	-

Types of Workers

1. Skilled mason
2. Labourer

Avg. daily wage (NRs.)

-/-
-/-

KEY CONTACTS

Municipal Office

LawSher Bist
Mayor
9855067692

Municipal Office

Er.Laxman dhakal
Focal Person
9845615021

Municipal Office

Khadka Bdr. Gopali
Deputy Mayor
9855067045

DLPIU-GMaLI

Bimal Kishor KP
Acting DLPIU-Chief
9855030632

Municipal Office

Hari Lal Puri
Chief Administration Officer
9855012111

DLPIU-Building

Sudip Achrya
DLPIU-Chief
9851153206

HHs WITH LAND ISSUES

No Reported Land Issues

STATUS OF TECHNICAL STAFF


Staff	Available Nos.	Additional Req. Nos.
Engineers	-	-
Sub-Engineers	-	-
Asst. Sub-Engineers	-	-
Masons	- (7 days) - (50 days)	- (7 days) - (50 days)

Source: Municipal survey

MASON TRAINING


Trainings (# out of total required)

7 days Training



Reached


50 days Vocational Training



Remaining

Source: HRRP Analysis

TA ACTIVITIES MAP

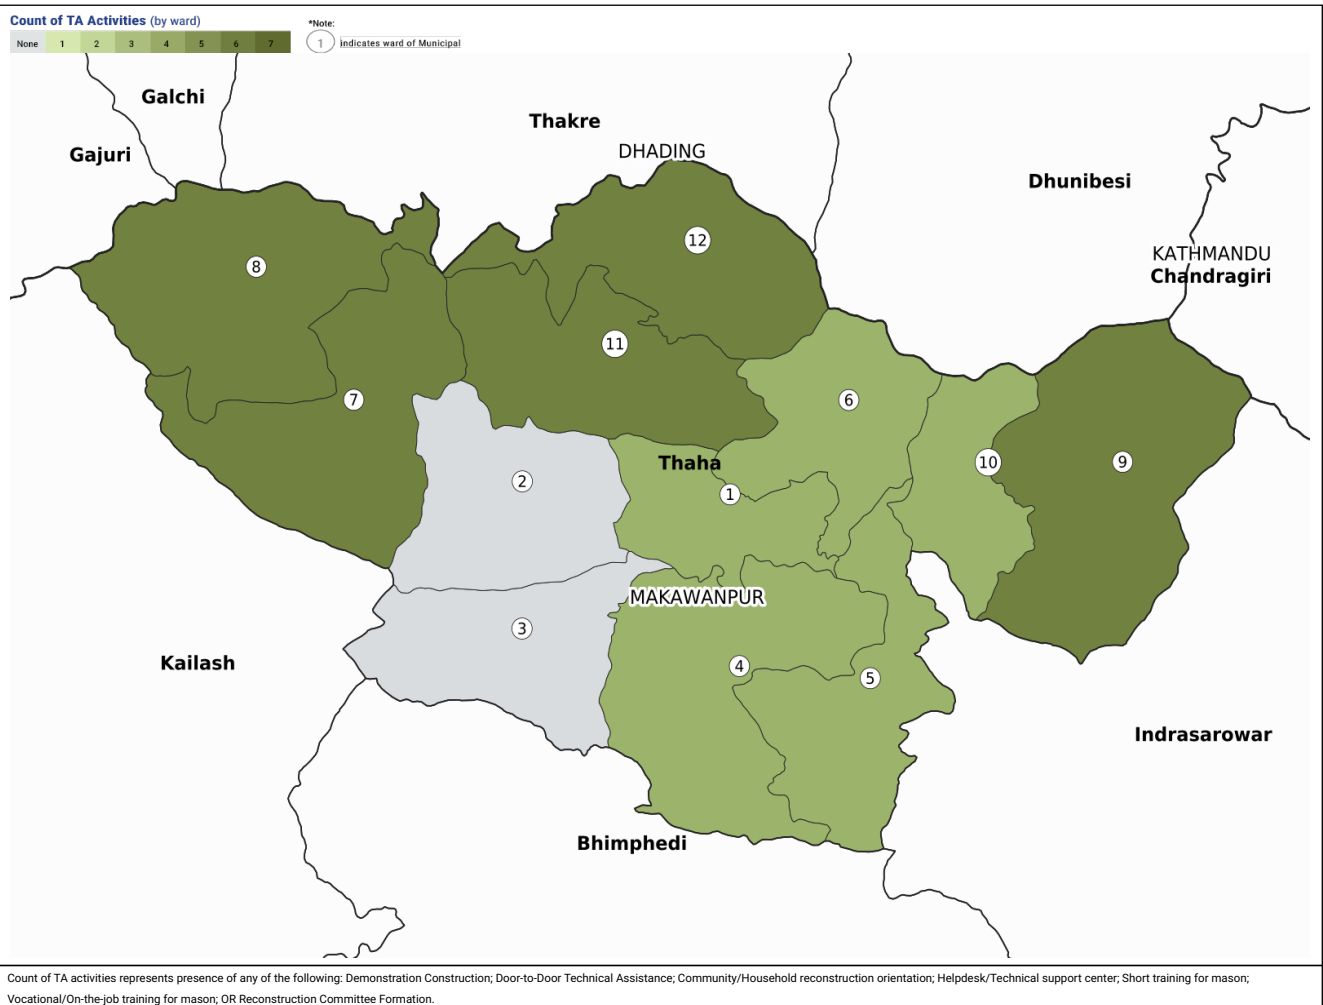

FAQs

Q: What documents are required for enrolment in the GoN housing reconstruction programme?

A: Two copies of passport size photos and original copy and photocopy of land ownership card and citizenship card. Local officials at the Rural / Urban Municipality will be able to provide information and support and households can enrol at the Rural / Urban Municipality.

Q: Do we need to pay the engineers when they come to conduct inspections or provide technical assistance?

A: No, you do not have to pay the engineers, or any other staff, conducting inspections or providing technical assistance. If any field staff request payment for conducting inspection or providing technical assistance you should report it to the Rural / Urban Municipality officials.

For further information 1. (General Coordinator) 2. Kausal Bist (Technical Coordinator) 3. Sachin Malego (Information Management Officer)
9849787273 984166793
